


Water Treatment Facility Advanced Process Improvement

April 2021

The Water Treatment Facility is staffed 24/7/365. For inquires or construction-related emergencies, please call (320) 255-7225.

CONSTRUCTION PROGRESS

The ozone destruction room walls were formed and poured, and will be buried as it previously appeared when completed. Piping to carry ozone through the building is double walled welded stainless steel. Each 20 foot section of pipe weighs approximately 700 pounds. A dewatering dumpster has been brought onsite to control the groundwater, while footings are poured. A dewatering dumpster removes sediment allowing the clean water to be safely put into the Mississippi River.

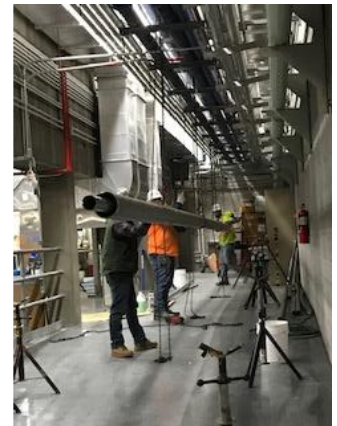

FAQs

A construction website was created. The website has additional project information. Please use this link.

<https://ci.stcloud.mn.us/WaterProject>

The Webcam link is also on the Construction Website. Please click on that link for a live look at the construction project.



How will you secure the construction site?

Additional signage has been placed. **All pedestrian and biking traffic needs to stay on the sidewalk, this is an active construction zone.**

To learn more about St. Cloud's Drinking Water Treatment, please visit

<https://ci.stcloud.mn.us/343/Drinking-Water-Services>

